

WEST SHORE LAKE PONTCHARTRAIN STAKEHOLDER UPDATE

February 2026

Arielle Steers, P.E.

Project Manager

Lake Pontchartrain and Vicinity Branch

New Orleans District

U.S. Army Corps of Engineers



U.S. ARMY



US Army Corps
of Engineers®




AGENDA

- Maps
- Construction Status
- Construction Photos
- Pre-Construction Status
- Resiliency Study Update

<https://www.mvn.usace.army.mil/About/Projects/West-Shore-Lake-Pontchartrain/>

Features Under Design & Construction

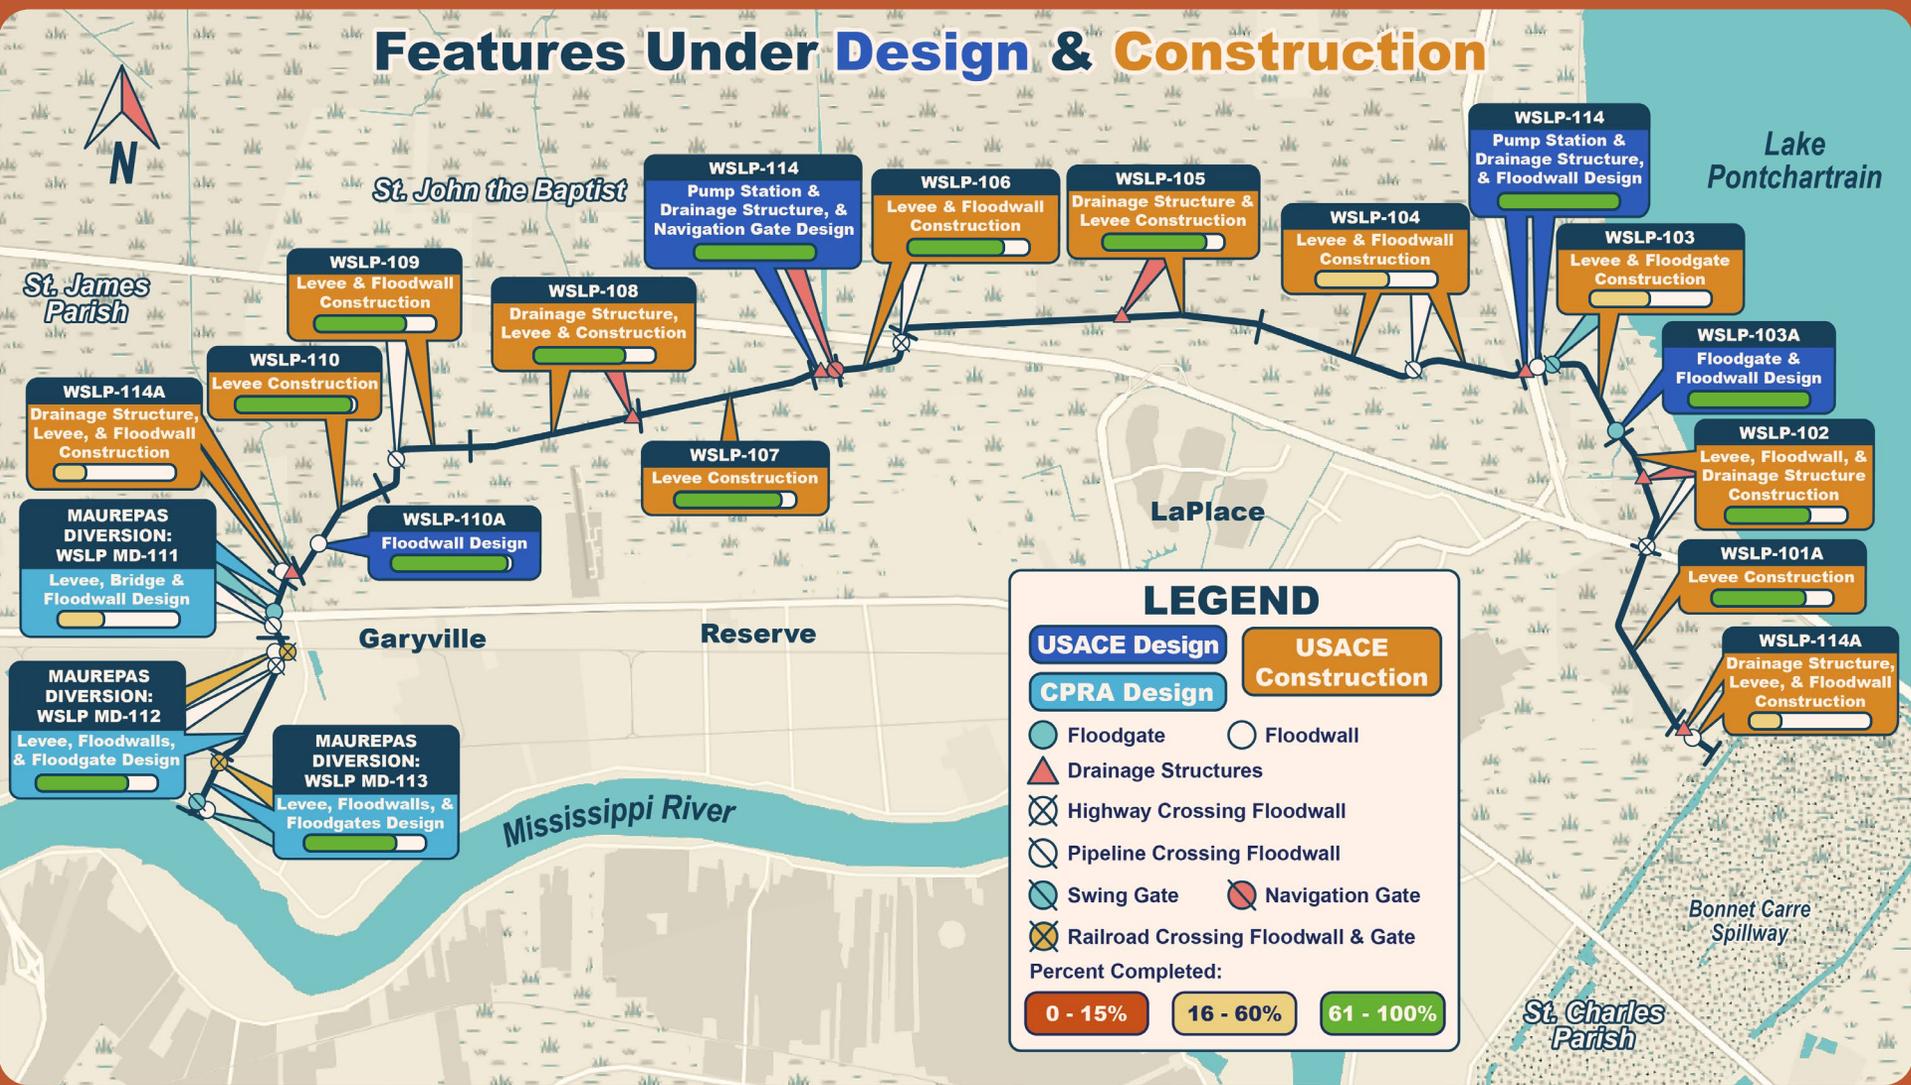

LEGEND


| | |
|---------------------|---------------------------|
| USACE Design | USACE Construction |
| CPRA Design | |

- Floodgate
- Floodwall
- Drainage Structures
- Highway Crossing Floodwall
- Pipeline Crossing Floodwall
- Swing Gate
- Navigation Gate
- Railroad Crossing Floodwall & Gate

Percent Completed:

| | | |
|---------|----------|-----------|
| 0 - 15% | 16 - 60% | 61 - 100% |
|---------|----------|-----------|

Funding Snapshot

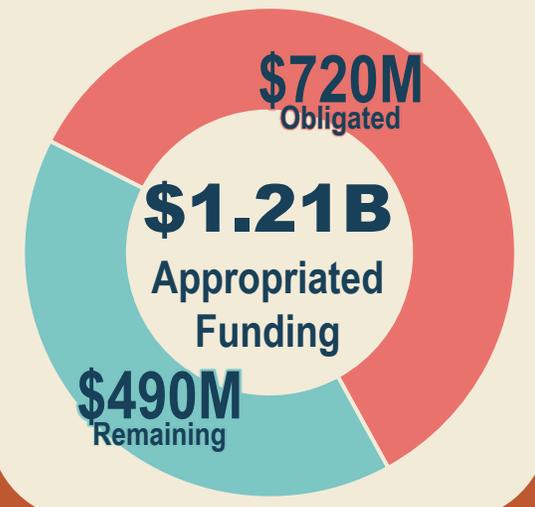


Future Capability





CONSTRUCTION STATUS

WSLP Construction Contract Schedule

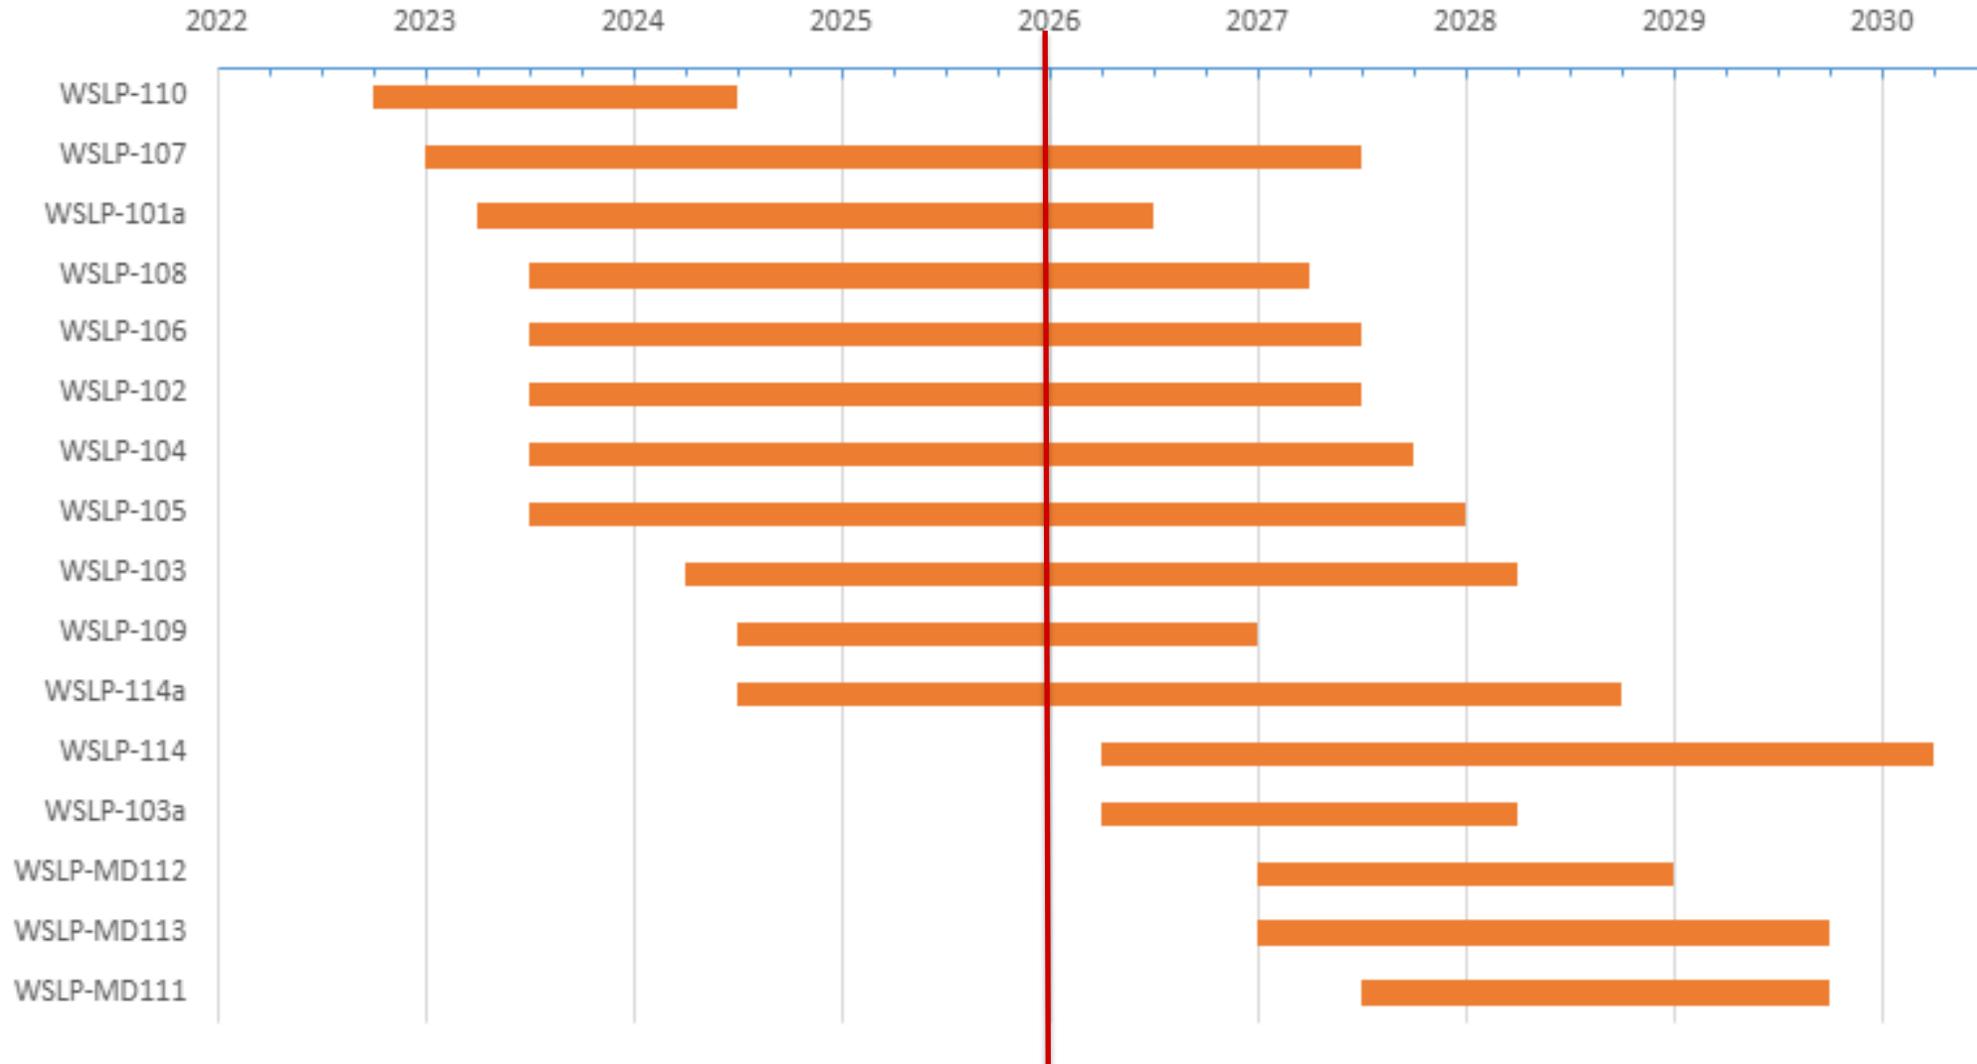


As of: Q1 2026

*Pump station contract – critical path



CONSTRUCTION STATUS

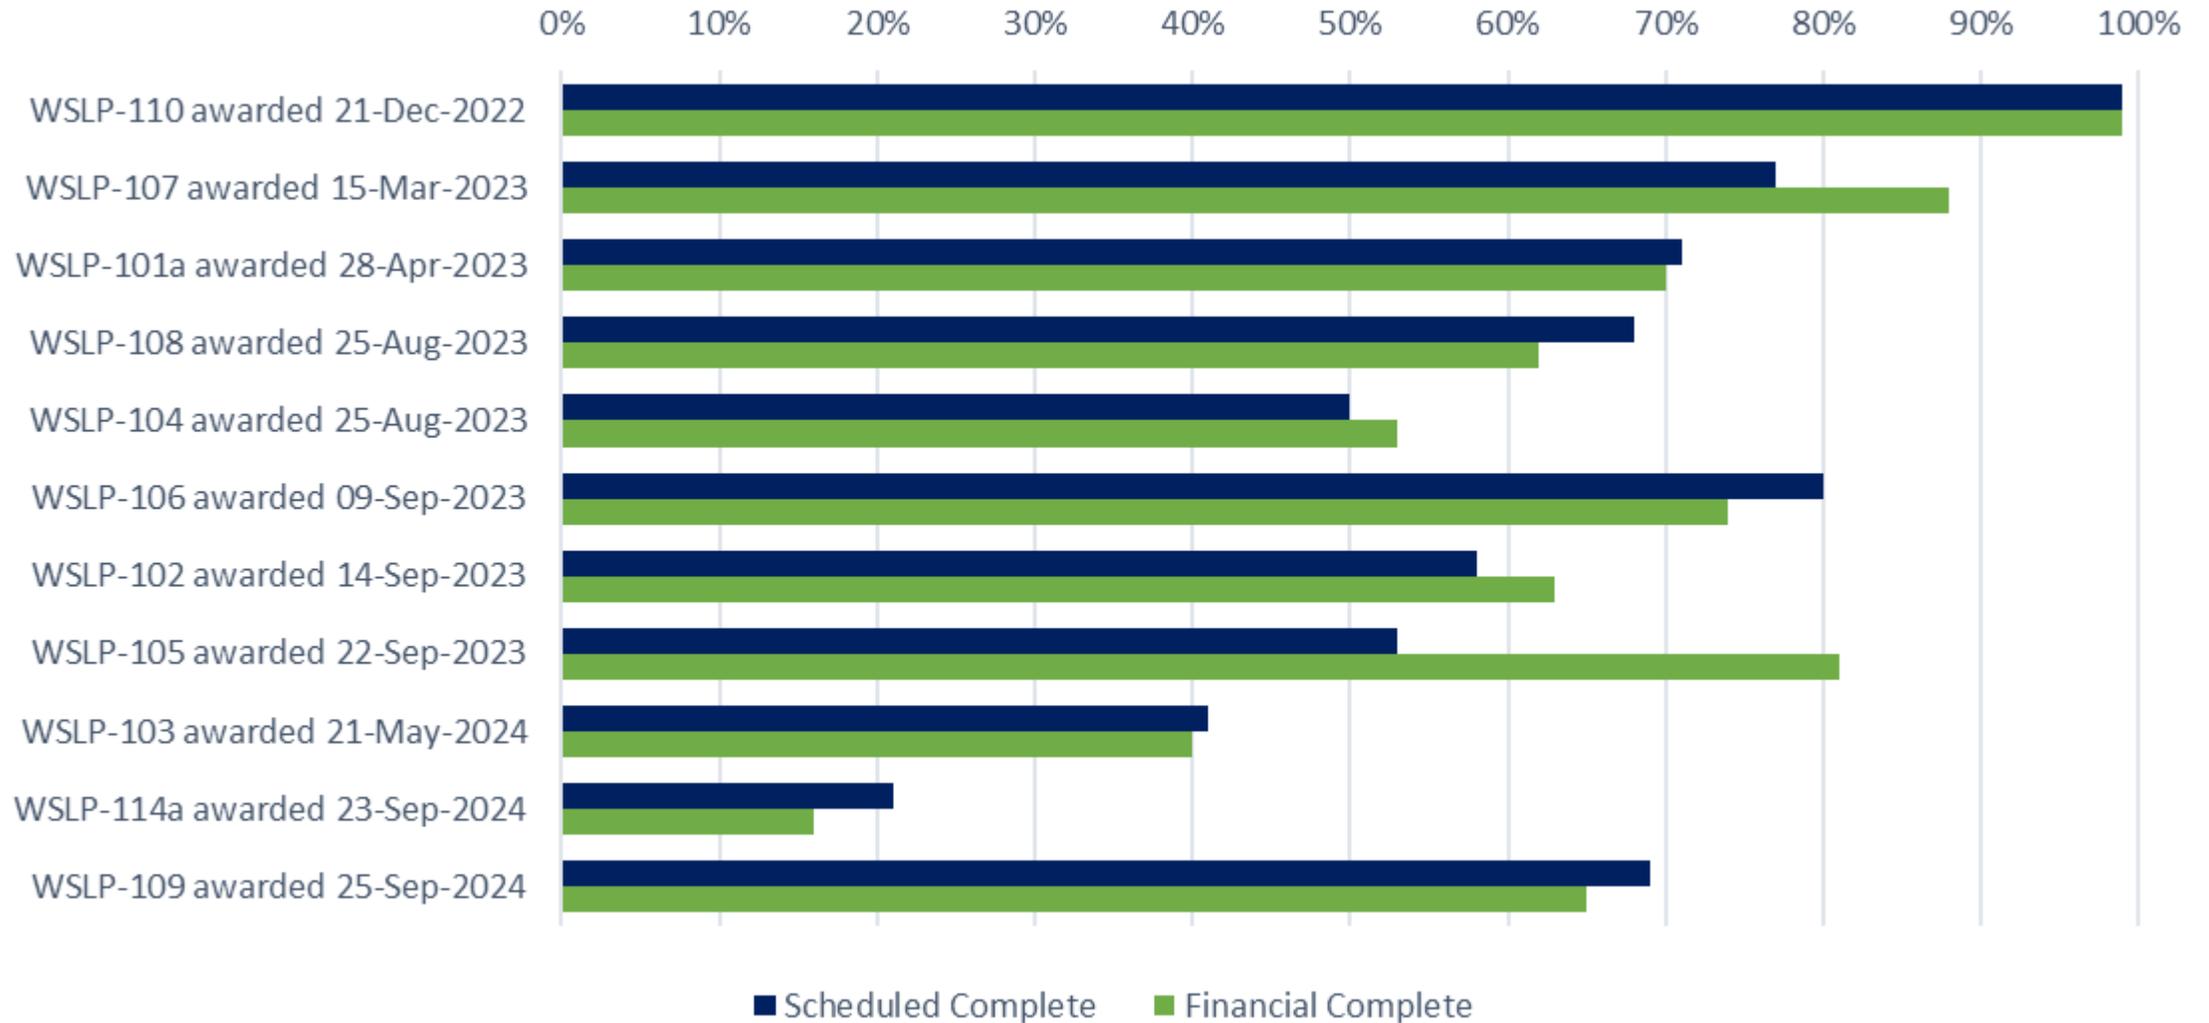

CONSTRUCTION PHOTOS



WSLP-101a Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-102 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-102 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-103 Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-104 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-104 Construction



U.S. ARMY
US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-105 Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-105 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-106 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-107 Construction



U.S. ARMY
US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-108 Construction



US Army Corps
of Engineers

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-109 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-110 Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-114a Construction



U.S. ARMY



US Army Corps
of Engineers®



PRE-CONSTRUCTION STATUS ST. CHARLES & ST. JOHN CONTRACTS

- **WSLP-114: Major Pump Stations and Drainage Structures**
 - Current Status: PLA exception received
No awardable bids at 6 Feb Bid Opening
 - Contract Award: Pending evaluation of cost estimates and bids

- **WSLP-103a: Frenier Floodgates**
 - Current Status: Working through P&S Approval
 - Contract Advertised: March 2026
 - Contract Award: May 2026

- **WSLP-110a: Air Products T-Wall**
 - Current Status: 95% P&S Complete
 - Contract Advertised: August 2027
 - Contract Award: October 2027



PRE-CONSTRUCTION STATUS MAUREPAS DIVERSION CONTRACTS AWARDED BY CPRA



- **WSLP-111: Levee from US-61 Raised Hwy Crossing to KCS RR**
 - Current Status: 35% P&S Complete
 - Contract Advertised: May 2027
 - Contract Award: August 2027

- **WSLP-112: Levee from KCS RR to CN RR**
 - Current Status: 65% P&S Complete
 - Contract Advertised: October 2026
 - Contract Award: January 2027

- **WSLP-113: Levee from CN RR to Mississippi River Levee Tie-In at River Road**
 - Current Status: 65% P&S Complete
 - Contract Advertised: October 2026
 - Contract Award: January 2027



PRE-CONSTRUCTION STATUS ST. JAMES CONTRACTS

- Identified initial contracts:
 - **WSLP-201: Gramercy Levee**
 - **WSLP-202: Grand Point Levee**
- USACE is evaluating options to the authorized project in St. James based on optimizing constructability and cost and responding to changing site conditions: St. James Parish applied for and was approved for a permit to build a levee and water control structures along the M2 Canal.



White: Authorized Project
Yellow: Current Option Being Evaluated
Purple: St. James Parish Connector Levee



RESILIENCY STUDY UPDATE

- As the PDT continued evaluating alternatives to incorporate the Parish's connector levee it was determined that changes to the authorized features in St. James could be considered under an Engineering Design Report rather than a study.
- As a result, the PDT has recommended termination of the study.



Questions



US Army Corps
of Engineers

U.S. ARMY

